

BARRAUD PARK PUMP STATION 153 PHASE 1

Project Manager: Selo Qejvani, 664-6773
Consultant: Clark Nexsen
Construction Inspector: Jamal Dean, 621-5216
Supervisor: Lawrence Paulmino, 646-4219

Project Scope: Design and construction of a wastewater pump station to serve Barraud Park.

PROJECT BUDGET: \$2,500,000

PROJECT STATUS

Planning: 100% complete
Design: 100% complete
Construction: 59% complete

Project Schedule


Design Completion: Summer 2015
Construction Start: Winter 2015/2016
Construction Completion: Winter 2016/2017

CONTRACT:

Advertised: May 10, 2015
Awarded: September 14, 2015
Contractor: Shaw Construction
Contract Amount: \$2,142,400

COMMUNITY CONNECTION:

Civic League: Barraud Park
Ward/Super ward: 3, 7

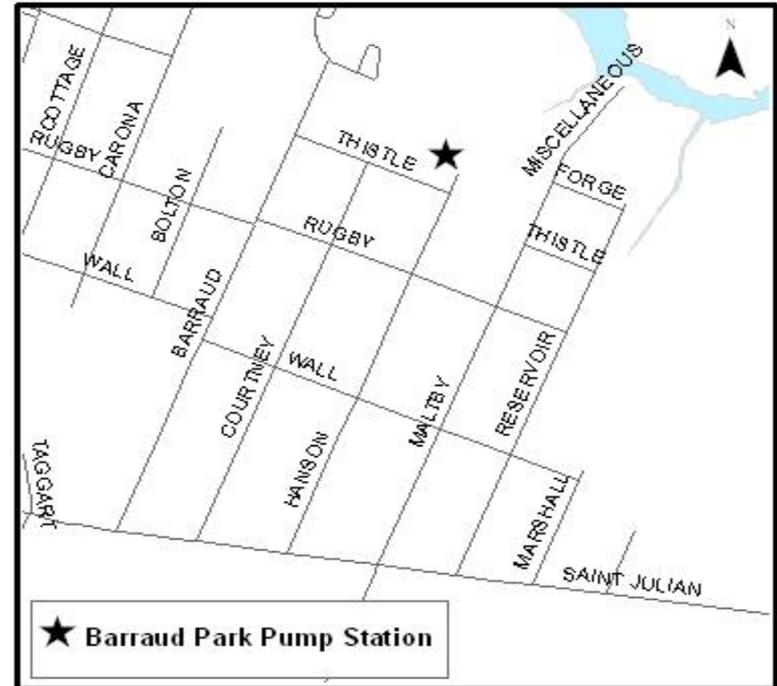

NOTES: Bruce's Park Civic League Meeting on Thursday, October, 27 and Barraud Park Civic League Meeting on Tuesday, October 11, 2016.
Project Bulletin: Dated September 2, 2015; work begins in winter 2015/16 and is finished by winter 2016/17

CO#1: Sacrificial sheeting to address west side soils instability (Estimate \$88,000)

Last updated: 10/2016
