

BRUCE'S PARK PUMP STATION 152, PHASE 2 (VRA)

Project Manager: Selo Qejvani, 664-6773
Consultant: Clark Nexsen
Construction Inspector: Lawrence Paulmino, 646-4219
Supervisor: Lawrence Paulmino, 646-4219

Project Scope: Sewer gravity main and water main replacement.

PROJECT BUDGET: \$1,200,000

PROJECT STATUS

Planning: 100% complete
Design: 100% complete
Construction: 99.9% complete

Project Schedule


Design Completion: Summer 2014
Construction Start: Winter 2014/2015
Construction Completion: Summer 2016

CONTRACT:

Advertised: August 3, 2014
Awarded: November 19, 2014
Contractor: Kevcor
Contract Amount: \$1,290,534

COMMUNITY CONNECTION:

Civic League: Bruce's Park
Ward/Super ward: 3, 7

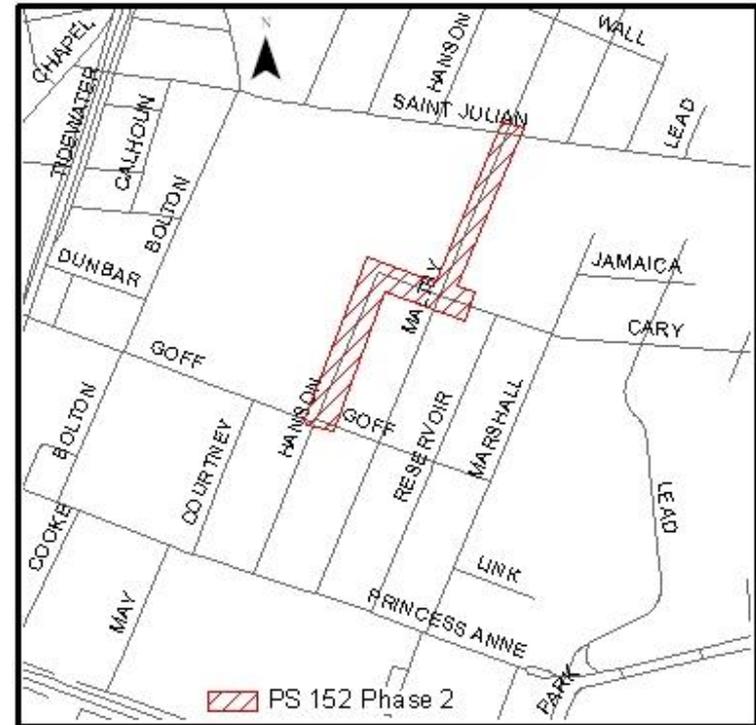

NOTES: Bruce's Park Civic League Meeting on Thursday, October 27 and Barraud Park Civic League Meeting on Tuesday, October 11, 2016.

Project Bulletin: Dated October 15, 2014; work begins in early 2015 and is completed by spring 2016.

CO#1: Sewer bypassing due to inclement weather and field changes; delays in phase one construction of pump station; installation of unforeseen storm drain structure \$81,250

CO#2: Quantities over contract line items.

Last updated: 10/2016
