

CONSOLIDATED COURTS COMPLEX


PROJECT TEAM

Project Manager: Tim McCrane
(Construction) (757) 664-4630

Construction Inspector: Mike Smith

Design Team: Fentress Architects

Contractor: Archer Western

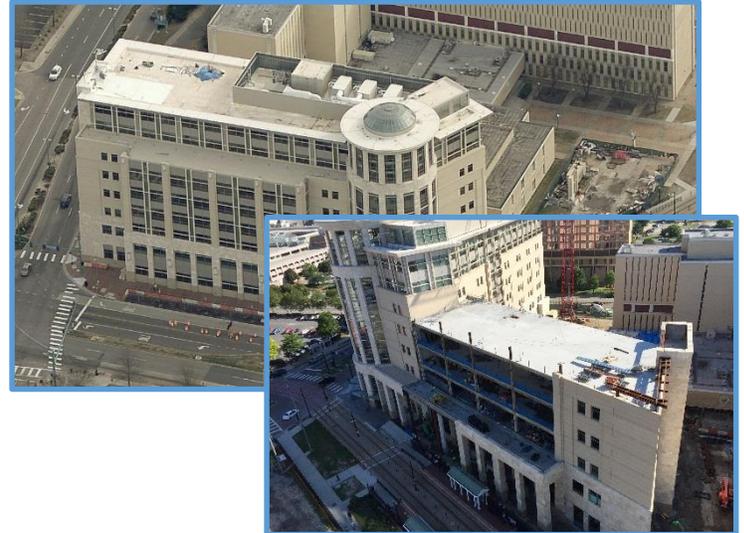

PROJECT DESCRIPTION: New multi-phase Norfolk Consolidated Courts Complex in new location.

PROJECT BUDGET: \$126,000,000

PROJECT STATUS

Planning: 100% Complete

Design: 100% Complete

Construction: 86% Complete

PROJECT SCHEDULE

Design Completion: 2014


Start of Construction: 2015

Construction Completion: Summer 2017

COMMUNITY CONNECTION

Civic League: None Affected

Ward / Superward: 4 / 7

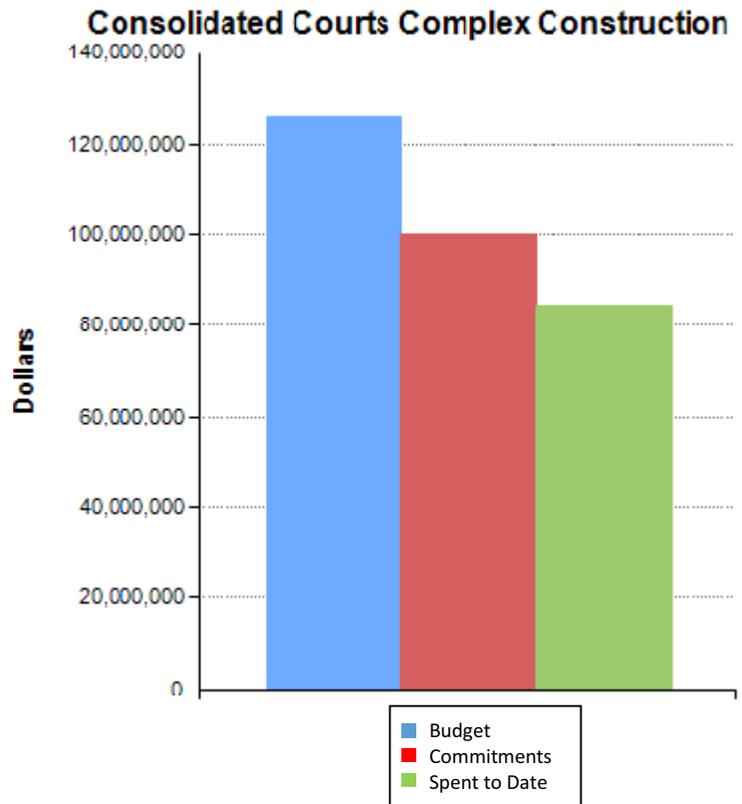

UPDATE: Phase 2 construction schedule remains at approximately 86% complete. The contractor is maintaining a Summer 2017 completion. The Phase 2 & 2A site work is approximately 30% complete.

LAST UPDATE: February 1, 2017

PROJECT NO: 05056
