

ARTS DISTRICT INFRASTRUCTURE IMPROVEMENTS

PROJECT TEAM

Project Manager: Chris Chambers (664-4693)
Construction Inspector: Not yet assigned
Construction Manager: Not yet assigned
Design Team: None
Contractor: None



PROJECT DESCRIPTION: With the goal of promoting safe, healthy and inclusive neighborhoods, this project provides infrastructure improvements to the Arts District

PROJECT BUDGET: \$200,000

PROJECT STATUS


Planning: 90% Complete
Design: 0% Complete
Construction: Not Yet Underway

PROJECT SCHEDULE

Design Completion: Fall / Winter 2016
Start of Construction: Spring 2017
Construction Completion: June 2017

COMMUNITY CONNECTION

Civic League: Downtown Norfolk Council
Ward / Superward: 2 / 6

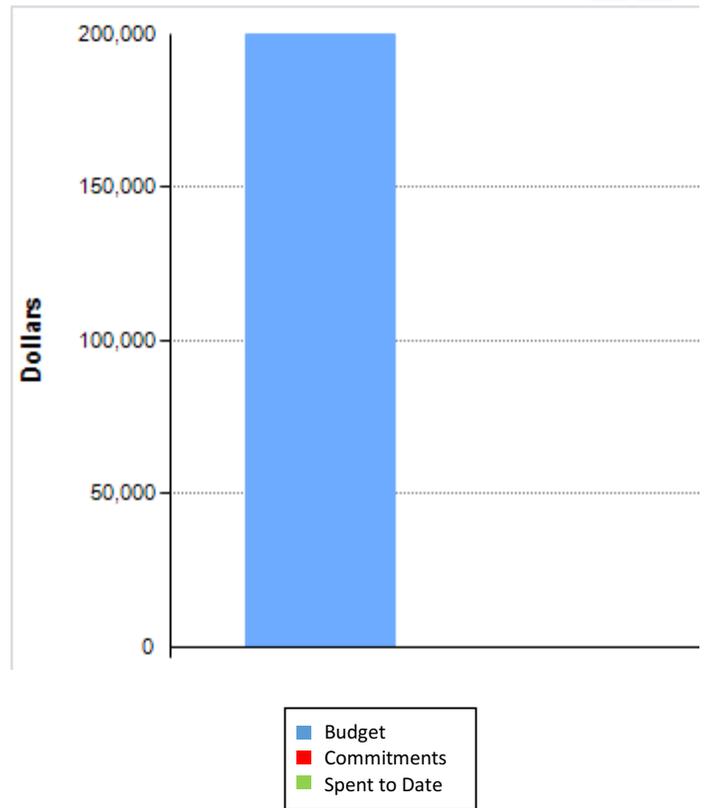

UPDATE: Wayfinding is highest priority of the Art District Committee, design is underway and construction will be complete in 2017. Funds are being transferred to DNC for installation of the wayfinding signs. Other priorities for future CIP funding are: extension of Arch lighting north of Brambleton Avenue; replacement of overhead street lights. adding pedestrian street lights, replacement of old sidewalks and the implementation of green infrastructure practices. To support these priorities streetscape standards are being developed.

LAST UPDATE: February 1, 2017

PROJECT NO: 16069
