


POPLAR HALL PEDESTRIAN IMPROVEMENTS

PROJECT TEAM

Project Manager: Dave Pfiffer (664-4638)
Construction Inspector: Jim Ellenburg
Construction Manager: Tyrone Walker
Design Team: Blakeway Engineers
Contractor: Site Work South



PROJECT DESCRIPTION: With the goal of promoting safe, healthy and inclusive neighborhoods, this project provides a safe pedestrian walkway located at the entrance to this community.

PROJECT BUDGET: \$250,000

PROJECT STATUS

Planning: 100% Complete
Design: 100% Complete
Construction: Underway




PROJECT SCHEDULE

Design Completion: June 2016
Start of Construction: December 2016
Construction Completion: Spring 2017

COMMUNITY CONNECTION

Civic League: Poplar Hall
Ward / Superward: 4/7

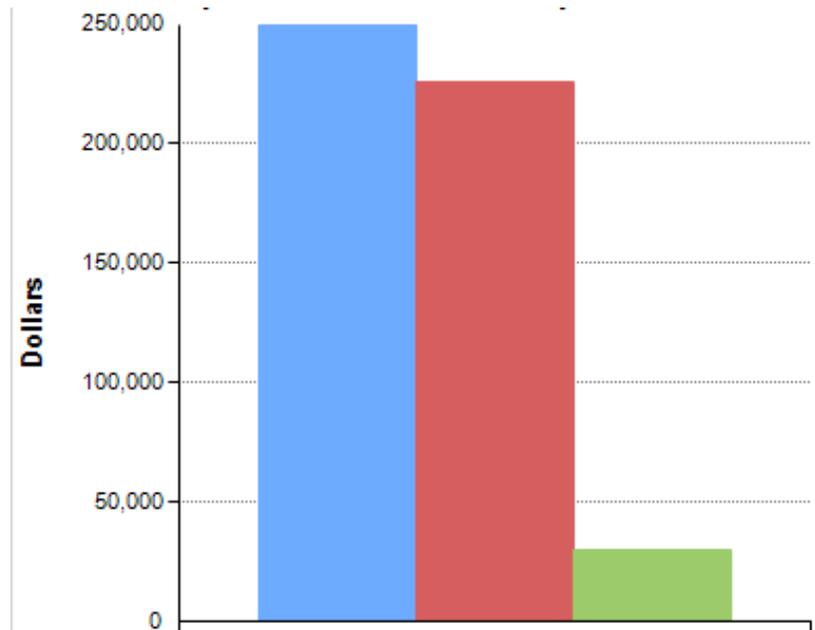

UPDATE: Construction fully underway, with work started on 4 of the 6 project medians, and some asphalt paving scheduled to take place in February 2017.

LAST UPDATE: February 1, 2017

