

# LINDENWOOD PUMP STATION 8 SERVICE AREA PHASE 7

## VRA

**Project Manager:** Selo Qejvani, 664-6773  
**Consultant:** Clark Nexsen  
**Construction Inspector:** Jose Arocho, 618-5575  
**Supervisor:** Calvin Lillard, 813-5451

**Project Scope:** Sewer gravity main and water main replacement.

**PROJECT BUDGET:** \$3,500,000

### PROJECT STATUS

Planning: 100% complete  
Design: 100% complete  
Construction: 0% complete

### Project Schedule


Design Completion: Summer 2016  
Construction Start: Winter 2016/2017  
Construction Completion: Winter 2017/2018

### CONTRACT:

Advertised: June 27, 2016  
Awarded: TBD  
Contractor: TBD  
Contract Amount: TBD

### COMMUNITY CONNECTION:

Civic League: Lindenwood  
Ward/Super ward: 3, 7

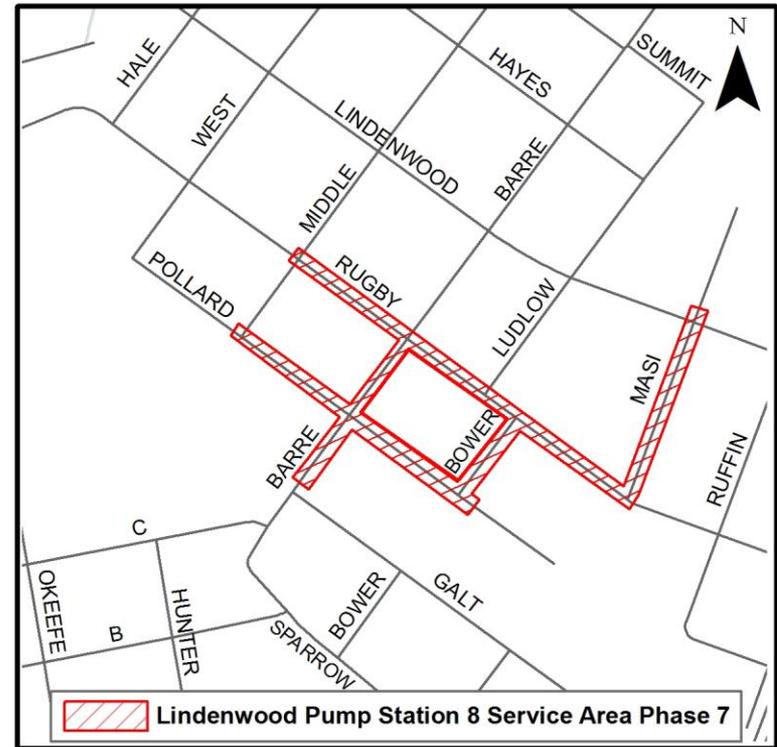

**NOTES:** Bruce's Park Civic League Meeting on Thursday, October 27 and Barraud Park Civic League Meeting on Tuesday, October 11, 2016.

Bid out on July 27, 2016: Apparent Lowest Bidder was W. R. Hall, \$2,987,185

Last updated: 10/2016
