

# MONTICELLO AVENUE WATER AND SEWER REPLACEMENT (DESIGN)

**Project Manager:** Leticia Quejada, 664-6768  
**Consultant:** RK & K 926-4588  
**Construction Inspector:** TBD  
**Supervisor:** TBD

**Project Scope:** Design and construction for the replacement of sanitary sewer and water mains along Monticello.

**PROJECT BUDGET:** \$113,994 (Design)  
\$1,000,000 (Const. Est.)

## **PROJECT STATUS:**

Planning: 100% complete  
Design: 60% complete  
Construction: 0% complete

## **PROJECT SCHEDULE:**


Design Completion: Spring 2017  
Construction Start: TBD  
Construction Completion: TBD

## **CONTRACT:**

Advertised: TBD  
Awarded: TBD  
Contractor: TBD  
Contract Amount: TBD

## **COMMUNITY CONNECTION:**

Civic Leagues: N/A  
Ward/Superward: 4/7

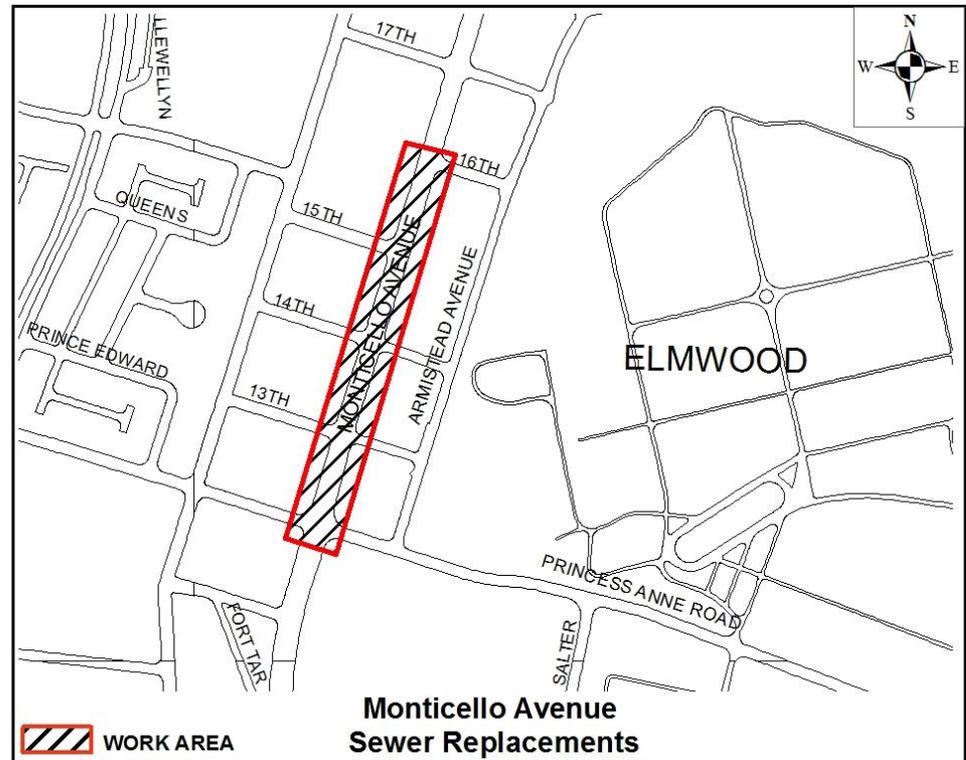

**NOTES:** Plans are being brought to bid ready status. Provide public notifications prior to bid advertisement.

Last updated: 10/2016
