

BAYVIEW PS 23 SERVICE AREA WATER & SEWER REPLACEMENT PHASE 4 – VRA

Project Manager: Leticia Quejada, 664-6768
Consultant: Hazen & Sawyer
Construction Inspector: Rhonda Wyda, 651-8433
Supervisor: Lawrence Paulmino, 646-4219

Project Scope: Replacement of sanitary sewer mains and water mains along Parkview Avenue from Densmore Place to Whit Avenue.

PROJECT BUDGET: \$1,552,406

PROJECT STATUS:

Planning: 100% complete
Design: 100% complete
Construction: 65% complete

PROJECT SCHEDULE:

Design Completion: Spring 2015
Construction Start: Spring 2016
Construction Completion: Winter 2016/2017


CONTRACT:

Advertised: June 2015
Awarded: September 2015
Contractor: Innerview

Contract Amount: \$1,552,406

COMMUNITY CONNECTION:

Civic League: Bayview Civic League
Ward/Super ward: 5 / 7

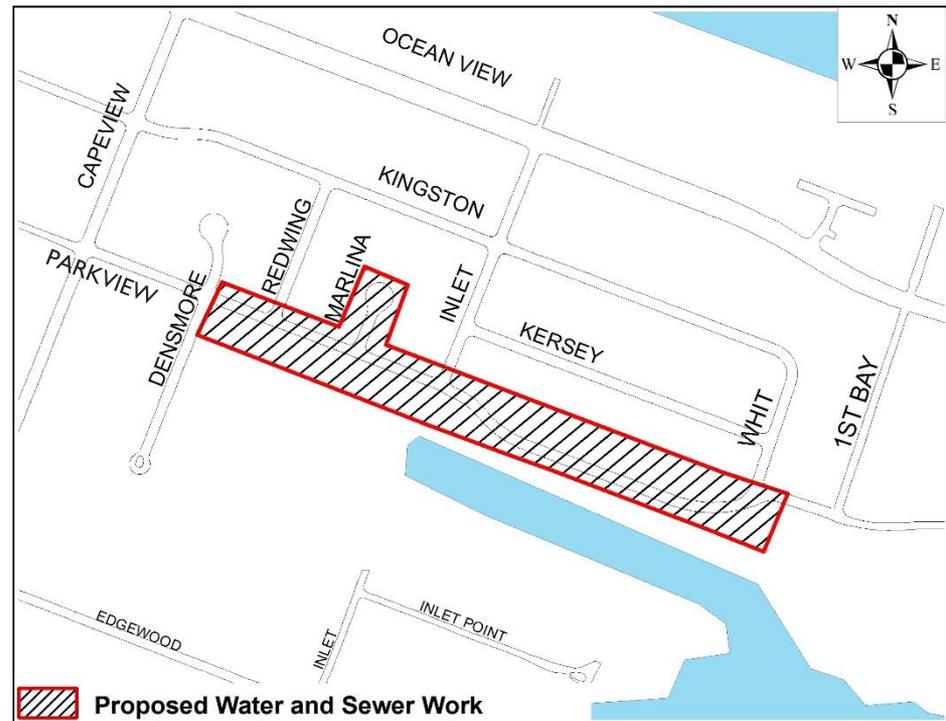

NOTES: Project bulletin was sent September 2015. Attended Civic League Meeting – June 14, 2016.

Last updated: 10/2016
