36" RAW WATER MAIN IMPROVEMENTS, SUPPORT & PIPE REPAIR AT AERIAL CROSSINGS 7, 16, & 26

Project Manager: Dan Riley, 664-6740
Consultant: M. Baker Jr. 463-8770
Construction Inspector: M. Baker Jr. 463-8770
Supervisor: Don Gartrell, 631-5427

Project Scope: Evaluation, Design, Repair/Replacement of raw main aerial support crossings.

PROJECT BUDGET: $103,604

PROJECT STATUS:

Planning:	100% complete
Design:	100% complete
Construction:	98% complete

PROJECT SCHEDULE:

Design Completion:	Spring 2015
Construction Start:	Fall 2015
Construction Completion:	Summer 2016

CONTRACT:

Advertised:	Spring 2015
Awarded:	Summer 2015
Contractor:	Earley Marine Inc.
Contract Amount:	$103,604

COMMUNITY CONNECTION:

NOTES: Coordination with the City of Portsmouth, City of Chesapeake, and the City of Suffolk.
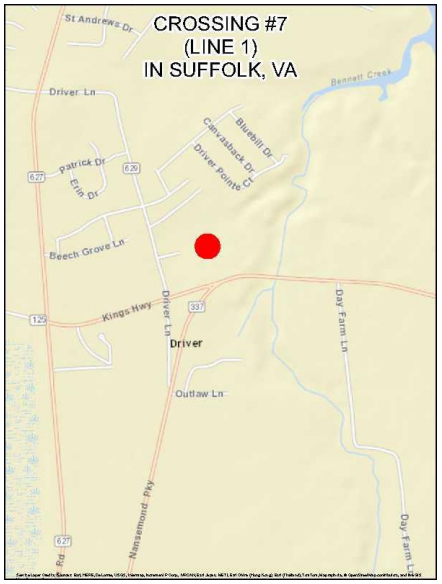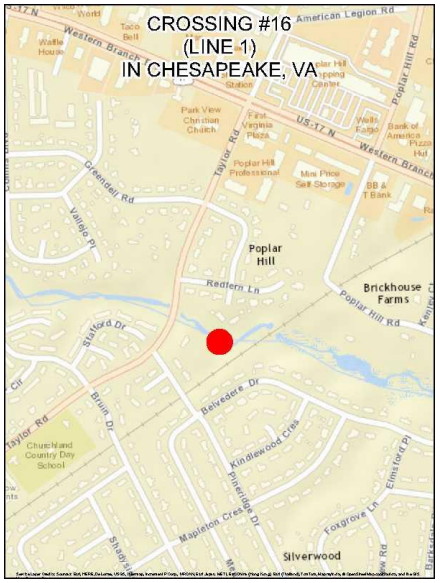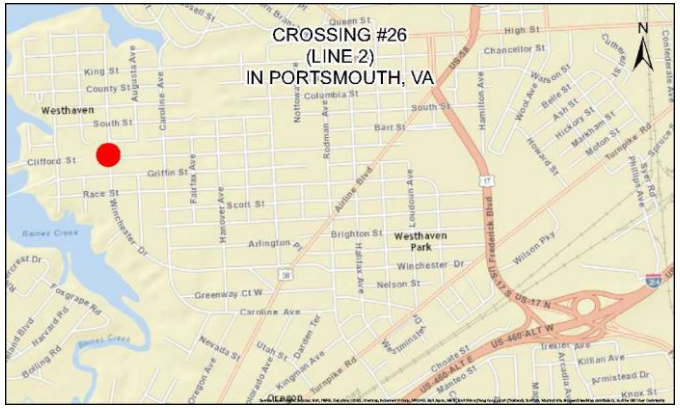
Last updated: 10/2016
