BAYVIEW PUMP STATION 23 SERVICE AREA WATER & SEWER REPLACEMENT PHASE 5 - VRA

Project Manager: Leticia Quejada, 664-6768
Consultant: Hazen & Sawyer
Construction Inspector: Rhonda Wyda, 651-8433
Supervisor: Lawrence Paulmino, 646-4219

Project Scope: Replacement of sanitary sewer force main, water mains, and sewer mains along Sunset Drive from Chesapeake Boulevard To Grove Avenue

PROJECT BUDGET: $2,175,407.50

PROJECT STATUS:
Planning: 100% complete
Design: 100% complete
Construction: 0% complete

PROJECT SCHEDULE:
Design Completion: Spring 2016
Construction Start: Winter 2016/2017
Construction Completion: Spring 2018

CONTRACT:
Advertised: July 17, 2016
Awarded: September 2016
Contractor: Peters and White Construction
Contract Amount: $2,175,407.50

COMMUNITY CONNECTION:
Civic League: Bayview Civic League
Ward/Super ward: 5 / 7

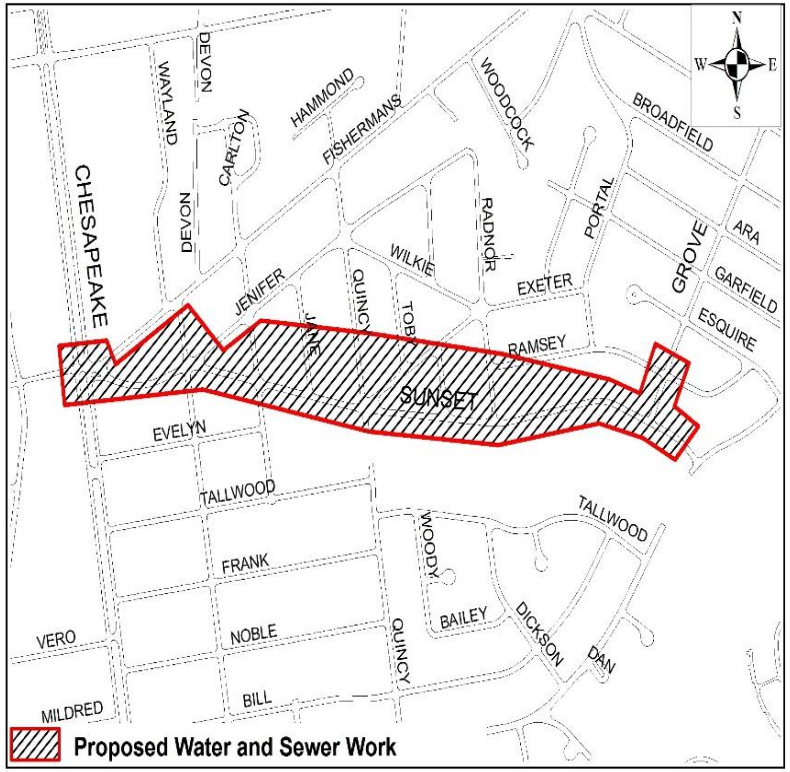

NOTES: Project bulletin was sent October 2015. Attended Civic League Meeting June 14, 2016.
Last updated: 10/2016
